


The background image shows a demolition site. In the foreground, there is a chain-link fence. Behind the fence, there is a large pile of debris, including wood, metal, and other building materials. In the background, there are several buildings that appear to be in the process of being demolished or are already partially destroyed. There are also some trees and utility poles visible in the distance. The overall scene is one of active demolition and cleanup.

Downtown Lindsay Demolition and Cleanup Project

Presented by Edna Hubbard and Baldo Rodriguez

Demolition and Cleanup Plan

1. Sawcut **braced walls** and **perimeter footing** separating portions of building to be demolished from the existing **common wall**.
2. **Demolish/dispose** of vertical structures
3. **Demolish/dispose** of slab and general debris

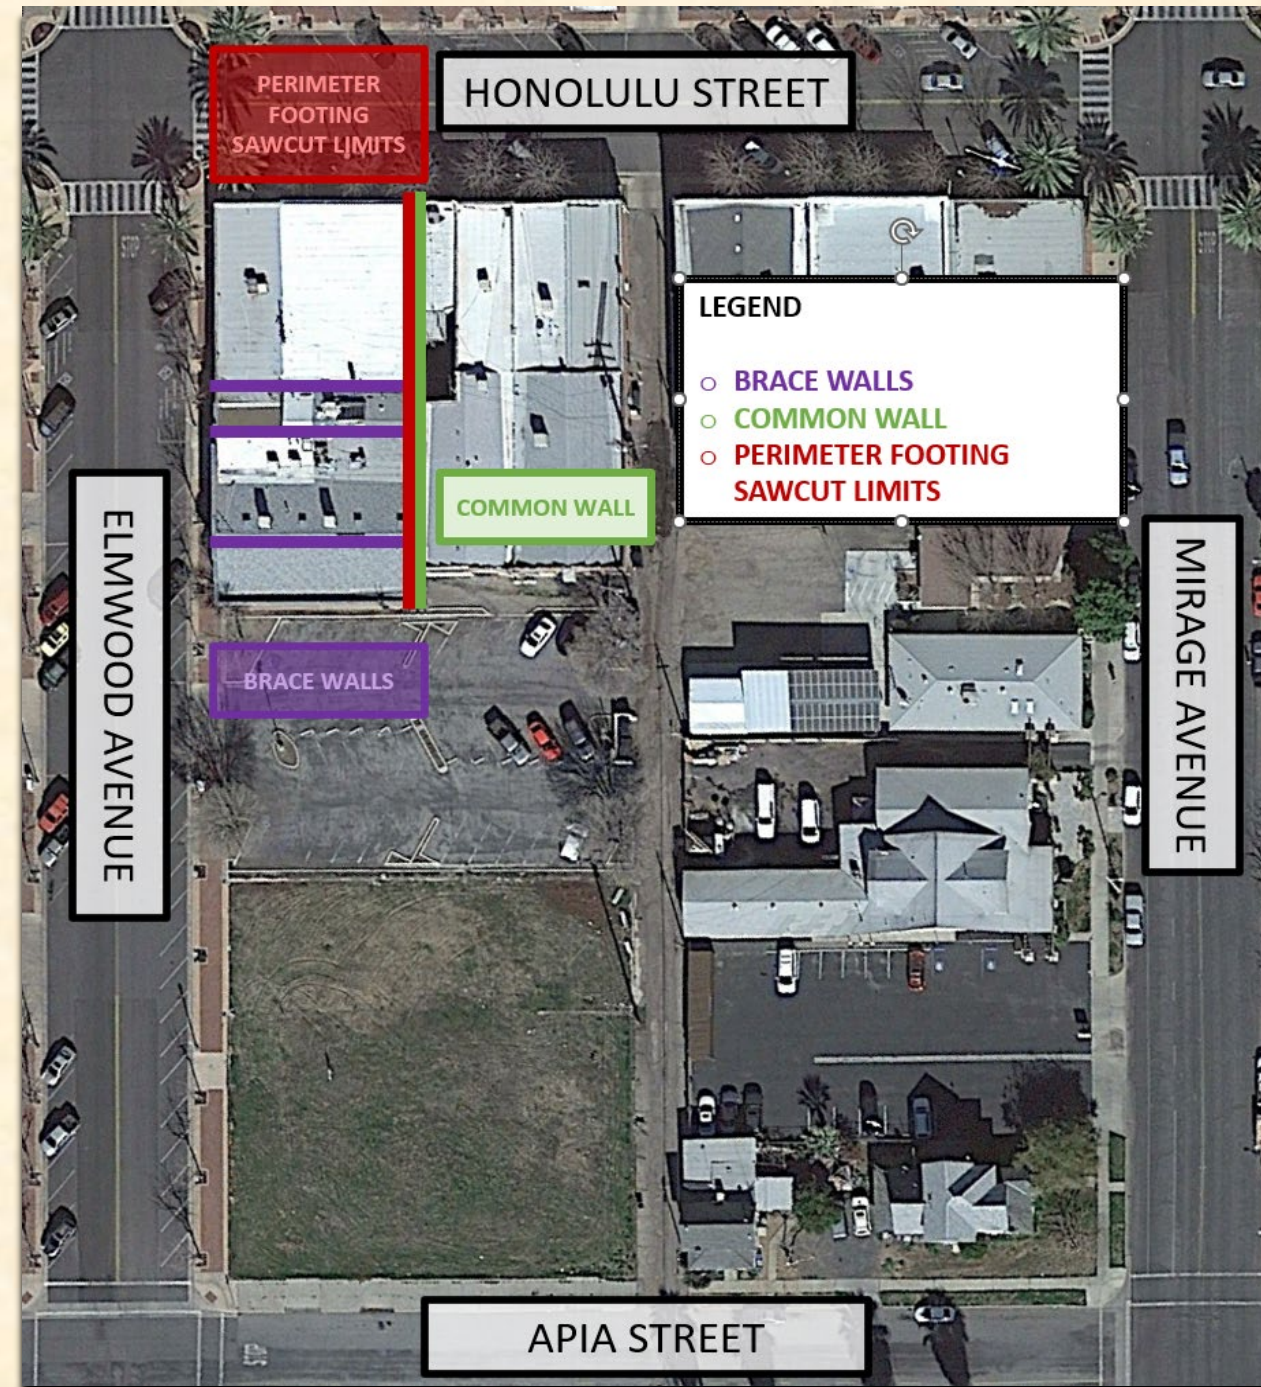

SITE BEFORE



Demolition and Cleanup Plan (Continued)

4. Demolish and dispose of top 2' of basement wall(s)
5. Break up basement slab to allow proper drainage of basement area
6. Over-excavate entire site approximately 2' deep, provide fill material, compact and grade site to drain away from common wall to Elmwood.
7. **Place and compact 3" of decomposed granite across entire project site.**

SITE AFTER



QUESTIONS?
